BRHAT BANGALORE MAHANAGARA PALIKE

INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Roads abd Drains at Anjanadri Layout Kattigenahalli in Ward No.05 Byatarayanapura Sub Division	
2	Estimate Cost	19.50 Lakhs	
3	Administrative Approved No and Date	94/13-14, Date. 07.08.2013	
4	Technical sanction No. and Date	02/13-14, Date. 12.08.2013	
5	Job Code No. and P Code No.	005-13-000039	
6	Tender Direct Entrested to KRIDL	Nil	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applicable	
8	Tender Approved Details	Not Applicable	
9	Work Order No and Date	671/2013-14, Date. 05.03.2014	
10	Stipulation time of Completion	60 Days	
11	Actiual Date of Commencement	23.08.2014	
12	Actiual Date of Completion	10.11.2014	
13	Delay if any	Nil Delay	

14	Reson for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verfied	Enclosed	
18	Date of Inspection	04.08.2015	
19	MB No. and Page No.	Mb No. 2572 Page No. 257233-44	
20	BR NO. and date	381/13-11-2014	
21	Test Result	Quality Test Report submitted by Civil Tech Consultents and Engineersis verified and Enclosed	
22	Section officer	Sri P A Chandrakanthraju A.E	
23	Sub Division Office	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
A	Work Quality	Satisfactory	
B	Comments	Work completed as per MB	

4/08/15

Executive Engineer
Byatarayanapura Division
Yalahanka Zone, B.B.M.P.
Bangalore-560092

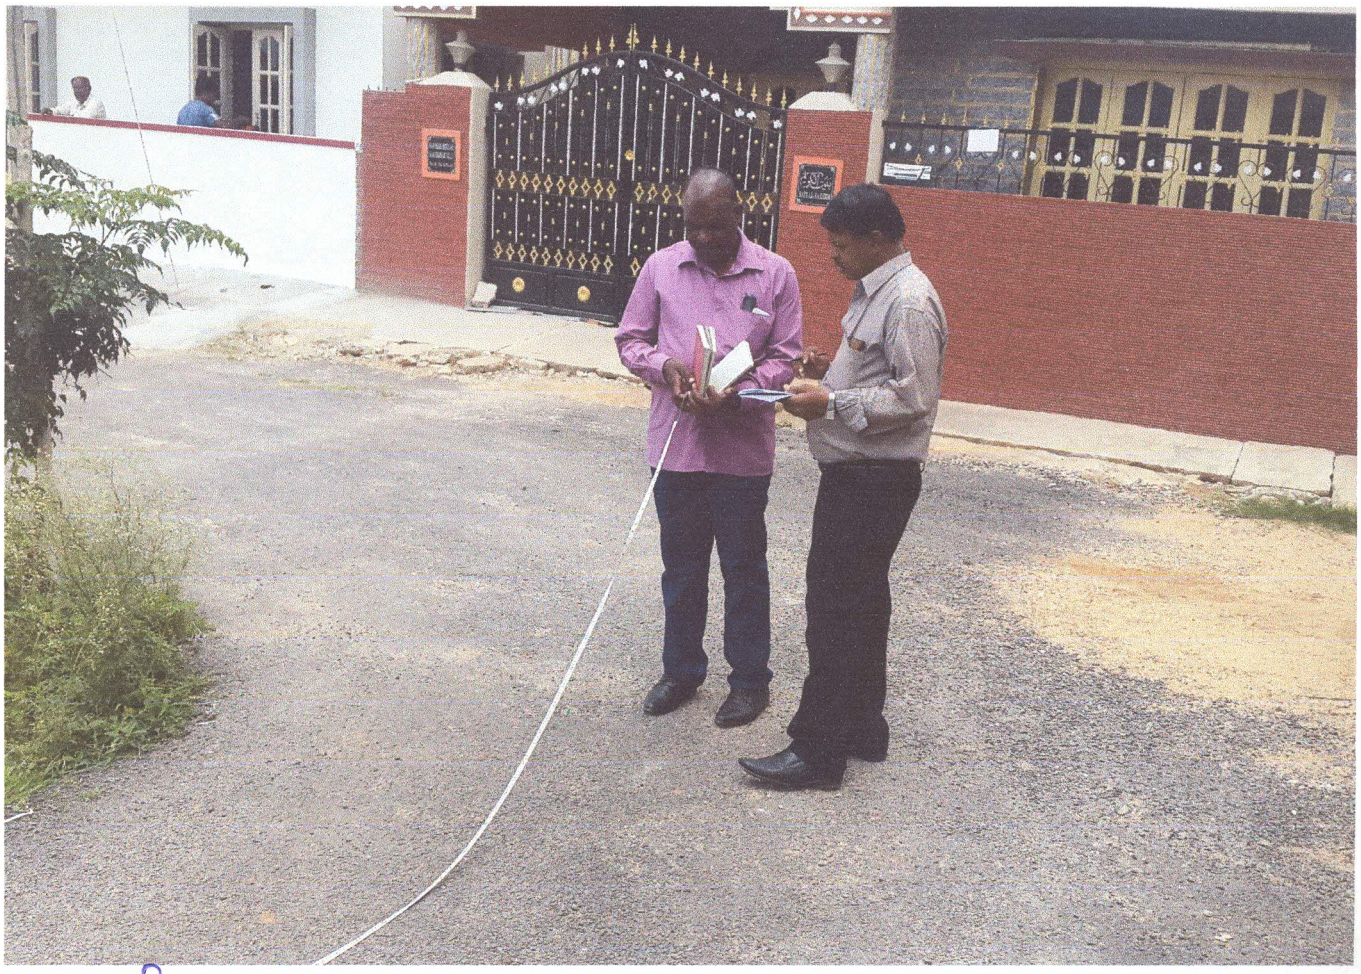

AE-05

AE-05

dy AE-01

AE-05
